

STC25 GR
Location

Opposite No. 64 Appletree Gardens

Year laid	Z	Status	PU	Function	F	Node type	M	Survey Date	22-Apr-2014		
COVER Shape	C	Hinge?	N	Lock?	N	Duty	H	Size	500	Toxic?	N
SHAFT S/E?	N	R/Courses	1	Depth	310			Size	580	Vermin?	N
CHAMBER Soffit	S	Steps	3	Ladders	-	Landings	-	Size	1060	Constr	P

Flow Depth	10	Silt Depth	-	Surch Depth	-	COVER LEVEL	40.605
------------	----	------------	---	-------------	---	-------------	--------

IN	Upstream MH Ref.	Pipe shape	Pipe Size	B/drop dia.	Pipe mat.	Lin. Mat.	Depth from cover	INVERT LEVEL
A	Private	C	150 x		VC		1.48	39.125
B	Private	C	150 x		VC		1.42	39.185
C			x					
D			x					
E			x					
F			x					

OUT	Upstream MH Ref.	Pipe shape	Pipe Size	Cond	Crit	Pipe mat.	Depth from cover	INVERT LEVEL
X	NZ3471 3301	C	225 x			VC	1.70	38.905
Y	NZ3471 4101	C	225 x			VC	1.58	39.025


Condition (Y if attn req'd)

Cover	N	Irons/lad	N	Shaft	N	Chamber	N	Benching	N	Other	N
-------	---	-----------	---	-------	---	---------	---	----------	---	-------	---

REMARKS Bifurcation Manhole

PHOTOS [Chamber](#)

LOCATION SKETCH

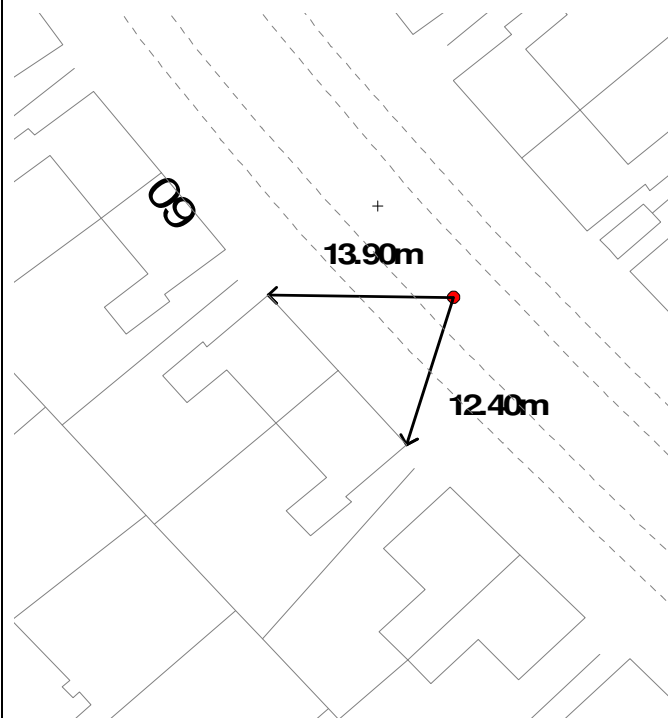

MANHOLE SKETCH

